



PNE Board Meeting

Masterplan Update
June 13, 2022

AMPHITHEATRE REDEVELOPMENT



PNE Amphitheatre




Progress updates

Item	Date	Status
City council approves Amphitheatre Renewal Project	June 2021	Complete
RFP (engineering and consulting services)	March 2022	Complete
Project Consultants awarded – Revery	April 2022	Complete
Consultants orientation and Project kick off	May 2022	Complete
Amphitheatre consultation (Inform Planning – as engagement specialist)	June-Nov 2022	On Target
Initial schematic design approval	Nov 2022	Targeted



DAYLIGHTED STREAM



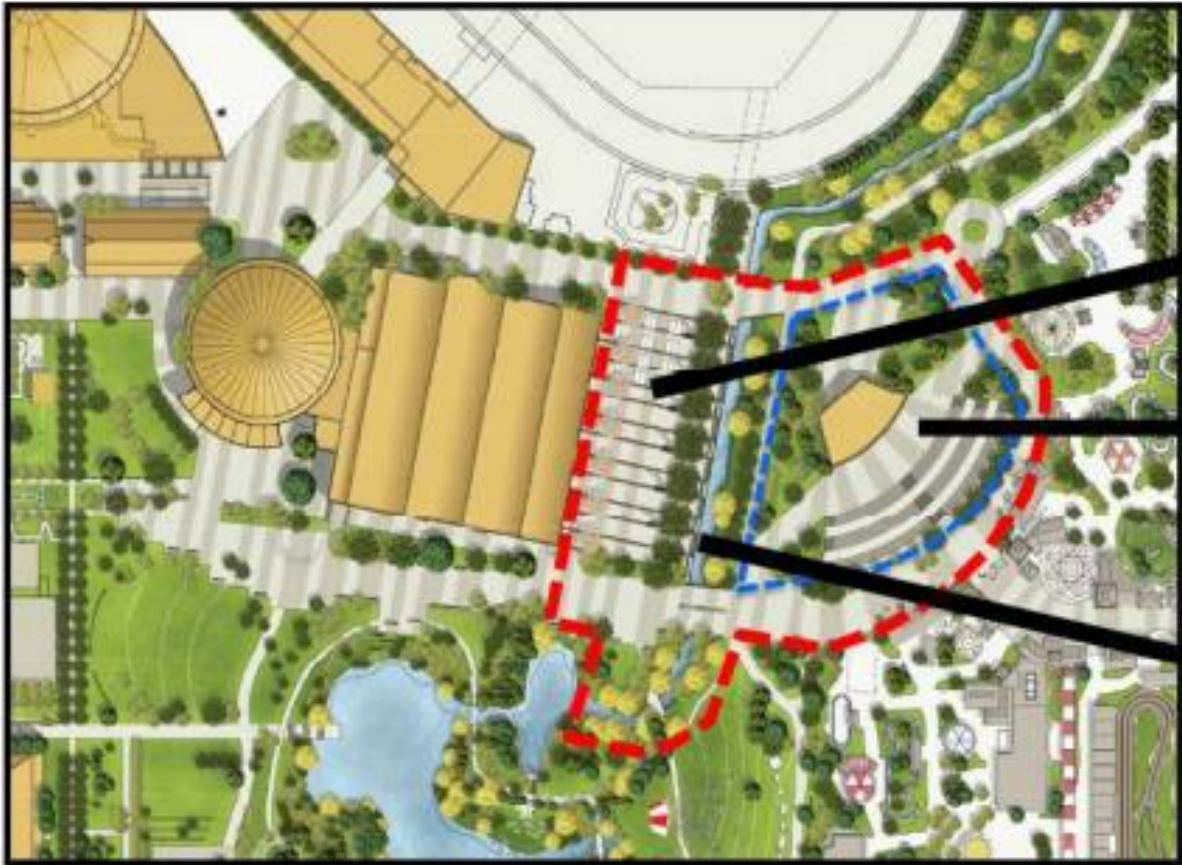

Festival Plaza

Amphitheatre

Daylighted Creek



Daylighted Stream

- ▶ Create an aquatic and terrestrial wetland with a strong focus on habitat, trails and boardwalks.
- ▶ Planning in parallel with Amphitheatre redevelopment project.
 - Environmental studies progressing concurrently.
- ▶ Initial step RFP (flow planning) targeted for July 2022
- ▶ Award contract August 2022
- ▶ Consultant onboard September 2022
- ▶ Vancouver Park Board leads the RFP process



INFRASTRUCTURE PROJECT



Infrastructure Masterplan

- ▶ Address and upgrade existing water, electrical and utility structure in support of overall masterplan, including Amphitheatre redevelopment, daylighted stream and Playland.

Phases of work	Date	Status
Develop Scope of Work – required electrical upgrades	June 2022	In Progress
RFP (planning, design and implementation)	July 2022	Pending
Onboard consultant	Sept. 2022	Pending

